

**SAN ONOFRE NUCLEAR GENERATING STATION (SONGS)
STEAM GENERATOR REPAIR TEAM (SGR_T)**

MEETING PURPOSE: 12/04/12 MHI-SCE Discussion on Technical Agreement Meeting

The purpose of this meeting is to discuss a technical agreement between SCE and MHI procurement / design path forward for long term repair schedules.

SUMMARY:

Discussion

- SCE proposed a straw schedule to MHI for discussion of a Technical / Commercial resolution (Attachment 1).
- SCE stated that time is of the essence, therefore, this straw was provided for discussion purposes to help put the overall project in perspective. SCE SGR is not discussing a commercial deal, only the technical framework.
- MHI missed the deliverable to SCE on 11/30/12 for the final repair type selection and also the technical presentation for the final repair on 12/04/12. These two missed deliverables put in jeopardy the CNO requirement to have a final recommendation (agreed to by MHI and SCE) to senior management by 12/28/12.
- SCE expressed concern that MHI had not discussed the potential to miss the deliverable due date based on an Non-Disclosure Agreement (NDA) until the due date at 0900. It was likely known before that date.
- SCE indicated to MHI that the technical team should continue working, independent of the NDA.
- SCE again emphasized that the CNO 12/28/12 deadline is for the final recommendation from SGR fully vetted out with MHI, not for the MHI deliverable to be provided to SGR.
- MHI indicated there is a 12/12/22 meeting between MHI senior management and P. Dietrich.
- SCE continues to maintain the 12/14/12 internal schedule date for review of the MHI proposed repair plan. SCE is developing the response based on knowledge of the options, however, will need the final submittal from MHI prior to issuance.
- SCE SGR looking to be in the Procurement Specification development stage in

**SAN ONOFRE NUCLEAR GENERATING STATION (SONGS)
STEAM GENERATOR REPAIR TEAM (SGR_T)**

first quarter, 2013.

- SCE asked if MHI was working on a proposed 'plan' for technical / commercial resolution (separate from the one provided by Ed). MHI indicated no, they were waiting for SCE to identify what is needed.
- SCE SGR is looking for MHI's feedback on the straw schedule (Attachment 1). Once feedback is received from MHI, SCE will talk to upper management.
- SCE reiterated that time is of essence.

Action Items:

- MHI to provide feedback on SCE's proposed schedule (Attachment 1).

Attachments: Attendees, Handouts


SAN ONOFRE NUCLEAR GENERATING STATION (SONGS)
STEAM GENERATOR REPAIR TEAM (SGR_T)
ATTACHMENT – Meeting Attendance Sheet
Discussion on Technical Agreement with MHI
Attendees
12/04/12

REDACTED

12/4/2012 1:16 PM

page 1

**SAN ONOFRE NUCLEAR GENERATING STATION (SONGS)
STEAM GENERATOR REPAIR TEAM (SGR_T)
ATTACHMENT 1 – Proposed Straw Schedule for Technical / Commercial Resolution**

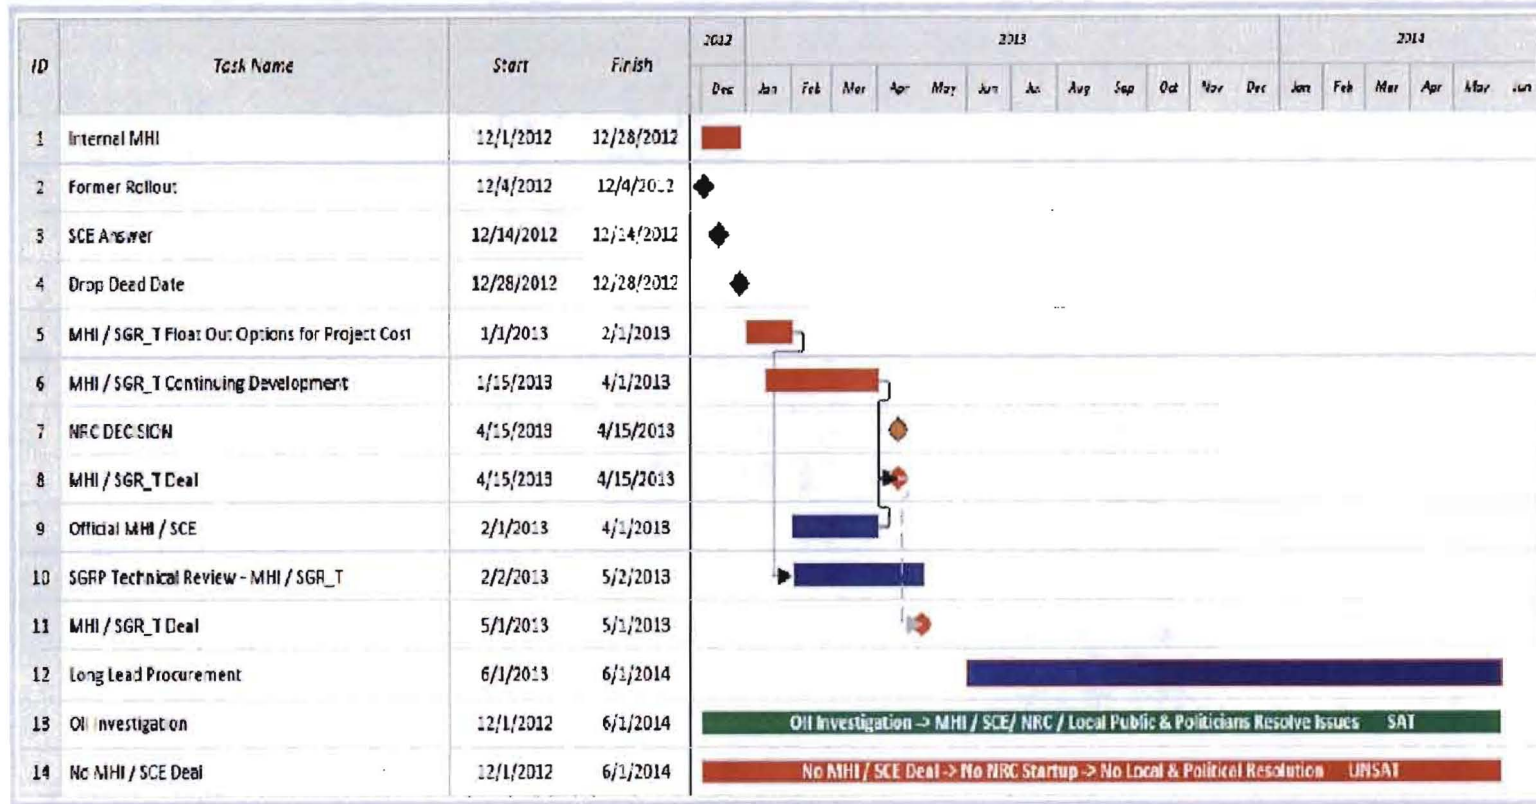

PLANT RETURN TO SERVICE
DECOMMISSIONING

TECHNICAL
COMMERCIAL

T-0 -> Repair Option 0 -> Stabilizers
T-1,2 -> Repair Option 1 & 2 -> Not Viable
T-3,4 -> Repair Option 3 & 4 -> Only Option

SGRP
4Q2016 -> 1Q2017
